

STEERING COMMITTEE BRIEFING

Ubuntu Capital OS

Turning stronger control into the first evidenced capability

The programme has materially reduced ambiguity and governance risk. The next leadership task is to convert that control into evidence-producing delivery - after one focused gate reassessment.

REPORTING WINDOW	26 AUG - 01 SEP 2026
BASELINE	master @ d2d6f7b
AUDIENCE	Ubuntu Capital OS Steering Committee
DOCUMENT	Internal working report

EXECUTIVE SIGNAL

A good week for control; a quieter week for capability

The programme is better governed, easier to reason about and safer to execute. That progress is real. It is also different from a deployed business outcome.



The sentence to carry into the room

Major reduction in delivery ambiguity and governance risk; limited movement in deployed business capability.

DIMENSION	CURRENT SIGNAL	STEERING INTERPRETATION
Programme	PARTIALLY_READY	Direction is credible; delivery evidence is not yet sufficient.
Architecture	READY_WITH_ASSUMPTIONS	Azure MVP baseline is selected, not proven in operation.
Production	NOT_READY	This is an honest control point, not a delivery failure.
Foundation Slice A	BLOCKED_BY_CONTEXT	Reassess the gate against the latest master baseline.

Leadership stance

Recognise the team's discipline. Avoid translating document volume into product progress. Authorise a short reassessment so delivery can move forward on evidence, not optimism or outdated blockers.

SEVEN-DAY MOVEMENT

The programme-control system matured meaningfully

Each improvement reduces a different kind of delivery friction: unreliable status, reopened architecture choices, unclear ownership or premature implementation.

1

Monitoring became more trustworthy

Impact detection now favours file-level evidence and suppresses broad-reference false positives.

2

Azure became a governed decision

The cloud baseline is explicit enough to estimate and assign without reopening platform selection.

3

Foundation became executable

WP-AZ-001 to WP-AZ-008 now have sequencing, acceptance, ownership and evidence conditions.

4

Governance stopped premature execution

The team separated 'ready to plan' from 'authorised to implement'.

5

Supplier accountability improved

Contributor provenance is clearer across HerLogic Solutions, Corefinity and 80K Developers.

6

The 41-use-case model became operational

Journeys, state models, integrations and structured use-case records were added.

7

Architecture assurance is active

Corefinity's solution architecture readiness review should be treated as a meaningful assurance gate.

Why this matters


For a private-markets platform, traceability is not administrative overhead. It is how the programme protects investor trust, supplier accountability and future regulatory assurance.

CURRENT TRUTH

Strong architecture position; early implementation position

The repository's status language is deliberately conservative. Steering should preserve that honesty while removing any blocker that the latest evidence has genuinely satisfied.

USE-CASE DELIVERY POSITION

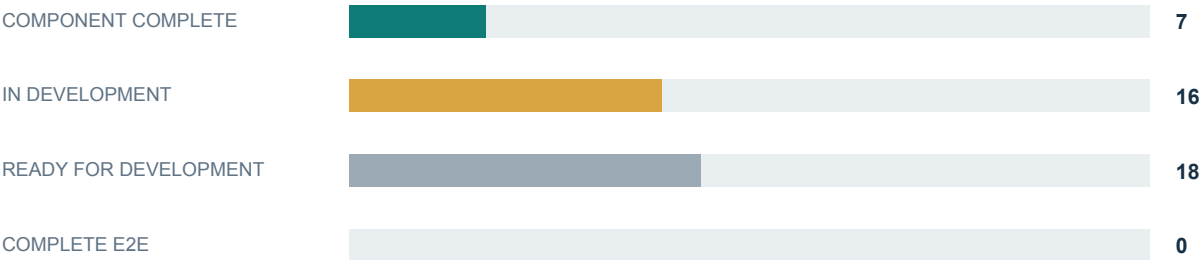

41 mapped use cases; UI evidence is not E2E business proof


WHAT IS TRUE	WHAT IS NOT YET PROVEN
41 use cases are mapped and increasingly machine-readable.	No use case has objective end-to-end completion evidence.
Seven items have UI/component-level evidence.	UI completion does not prove identity, rules, persistence, security or audit end to end.
The Azure MVP direction is explicit and governed.	The selected architecture is not evidence that Azure resources are deployed and integrated.

A pause at the gate is not a lack of momentum. It is evidence that the control system is working. The important question is whether the gate still reflects the newest baseline.

ARCHITECTURE DIRECTION

The platform choice is clear enough to execute

Static Web Apps, Entra External ID, Functions, SQL, Key Vault, Managed Identity and Azure monitoring form the confirmed MVP direction. Blob Storage remains selected but deferred until a business slice requires it.

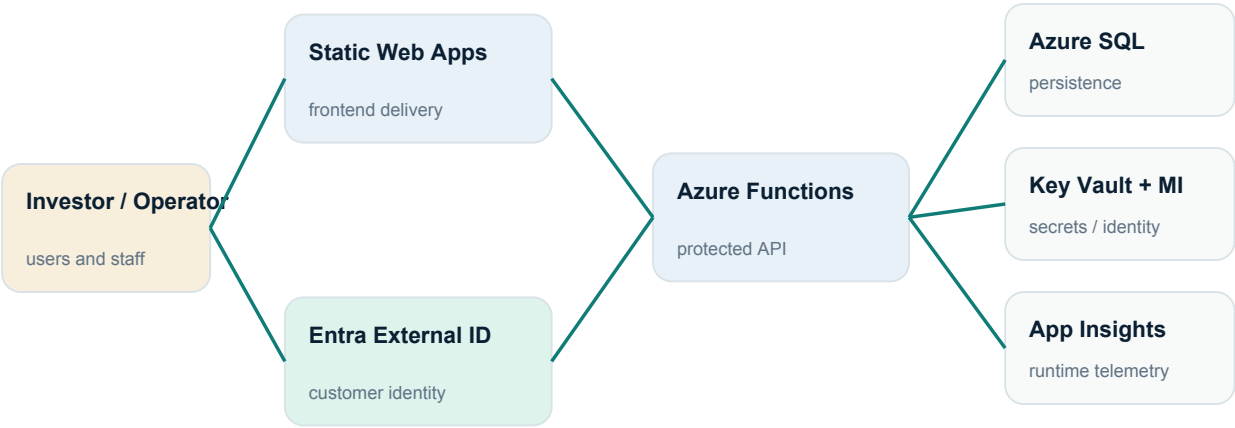

Selected target architecture. Deployment and integration evidence remain separate gates.

STEERING CONFIDENCE	ASSURANCE STILL REQUIRED
The team can estimate, sequence and assign Foundation work without reopening the cloud decision.	Identity enforcement, persistence, security, observability and reproducible deployment need objective evidence.
Architecture and domain boundaries are intentionally separated.	Critical legal, eligibility, NDA, custody and reporting rules remain business evidence dependencies.

Boundary to preserve

Foundation completion can prove the platform shell. It does not make an investment use case complete, and it does not resolve business or regulatory authority.

MANAGEMENT ISSUE

The gate may be directionally right but factually stale

The latest master commit added several artefacts that earlier roadmap language described as missing. The right response is neither to rush ahead nor to preserve a block by habit.

EARLIER CONTROL POSITION	LATEST REPOSITORY SIGNAL
Actors and permissions were identified as missing or misaligned.	actors.md and permissions-matrix.md now exist.
Journeys, state models and integrations were incomplete.	Machine-readable journeys.json, state-models.json and integrations.json now exist.
Use-case specifications needed stronger structure and traceability.	Structured use-cases.json and detailed catalogue specifications were added.

A focused gate reassessment should answer only three questions

QUESTION 1	Which Phase 0-4 blockers are genuinely still outstanding after d2d6f7b?
QUESTION 2	Which blockers are now satisfied by objective repository artefacts?
QUESTION 3	May WP-AZ-001 begin, or what exact residual item prevents authorisation?

Tone for the reassessment

Treat the earlier block as a responsible decision made with the evidence available at the time. Reassessment is good governance, not a reversal or a search for fault.

PEOPLE AND RISK

Protect momentum without rewarding premature certainty

A high-trust steering response recognises the work, keeps the truth intact and gives each contributor a fair route to closure.

SIGNAL	RISK	LEADERSHIP RESPONSE
YELLOW	Documentation velocity may outpace application delivery.	Time-box broad planning and prioritise evidence-producing implementation after the gate.
RED	README and roadmap statements may conflict with the newest artefacts.	Reconcile status language before authorising work; keep a named evidence record.
AMBER	Regulated-flow rules remain unverified in key areas.	Assign business authority for eligibility, KYC/AML, NDA, custody and reporting decisions.

What contributors need from the committee

Delivery team	A stable definition of the next evidence-producing outcome and permission to stop expanding the planning surface.
Architecture	A clear assurance role: validate residual dependencies without becoming the owner of business authority.
Contractors	Explicit deliverables, acceptance evidence and provenance - with contribution recognised without implying approval authority.
Business owners	Named decisions and response dates for regulated-flow questions that engineering cannot responsibly invent.

DECISION REQUESTED

Authorise a short gate reassessment, then pivot to evidence

This is a bounded decision. It does not authorise production, regulated transaction flows or work packages whose dependencies remain unresolved.

Recommended steering resolution

The Steering Committee acknowledges the material governance and architecture progress achieved during 26 August-1 September 2026; directs a time-boxed Pre-Implementation Gate Reassessment against master commit d2d6f7b; and authorises WP-AZ-001 to commence only if the reassessment records that all applicable start-gate conditions are satisfied.

WHEN	ACTION	EVIDENCE OF DONE
Days 1-2	Map every Phase 0-4 gate item to the latest artefact.	Signed gate checklist with CONFIRMED / UNKNOWN / CONTRADICTED status.
Day 3	Resolve status contradictions in README, roadmap and evidence register.	One canonical current-state statement at d2d6f7b or later.
Day 4	Record go / conditional go / no-go for WP-AZ-001.	Named approver, residual conditions and expiry/review date.
Days 5-10	If authorised, execute the smallest Foundation evidence increment.	Objective Azure baseline evidence entered in the Foundation register.

Success measures for the next report

1 CANONICAL GATE STATUS	0 UNEXPLAINED CONTRADICTIONS	1st OBJECTIVE DELIVERY EVIDENCE
---	--	---

The committee's most useful contribution now is clarity: one gate, one owner, one evidence-producing next step.

EVIDENCE NOTES

Basis, language and responsible interpretation

This report synthesises repository evidence and a project-management assessment. It does not claim live-system inspection, legal validation or production readiness.

SOURCE	HOW IT WAS USED
docs/engineering-sessions/2026-09-01-ubuntu-capital-os-reconstruction-session.md	Session baseline, governance model, status distinctions, risks and open questions.
Stakeholder project assessment supplied for 26 Aug-1 Sep 2026	Seven-day movement, PM scoring, commit/PR context and recommended reassessment.
README.md and docs/09-delivery/* at master d2d6f7b	Current repository status language, coverage counts, Foundation gate and Azure package definitions.

Evidence language used in the programme

CONFIRMED	Directly supported by repository or supplied evidence.
INFERRED	A reasoned conclusion that still needs direct validation.
UNKNOWN	Evidence is not yet sufficient to decide responsibly.
CONTRADICTED	Current sources make incompatible claims that require reconciliation.

Responsible reading

The PM ratings are directional judgements intended to aid discussion, not audited performance measures. PR #24 is described from the supplied assessment and should be verified in the repository workflow before being used as formal approval evidence.
